



# City of Owatonna – W. Bridge Street Reconstruction

Newsletter

June 25, 2021


Phase 1 work continued with the placement and compaction of additional aggregate for the road base. Riprap for the ends of the culverts is being brought onsite and placed. The purpose of the riprap is to provide energy dissipation and reduce the erosion effects from fast-moving stormwater. Alongside the riprap placement, the north road ditch is being fine-graded with topsoil in preparation for seeding.

Planned work next week will be additional road base preparation and turf establishment within the areas that have been graded to final elevations. Concrete paving is planned to begin on July 12<sup>th</sup>.

Traffic changes are also anticipated to be implemented as Phases 1A and 1B begin. Work on Phase 1A is scheduled to begin on July 6<sup>th</sup> and Phase 1B is planned for July 12<sup>th</sup> to coincide with the concrete paving schedule. Additional media releases and revised detour routes will be provided next week.

This project is phased and is anticipated to generally follow the phasing plan as shown in the image below. Currently, the contractor is working in the “Construction Phase 1” area as outlined in blue. Following Phase 1, work is expected to take place within Construction Phases 1A and 1B (shown in pink and orange) at which time, detour routes will be adjusted.

Please feel welcome to contact Reese Sudtelgte or Anthony Lance of ISG with any questions regarding the project or any other items of concern.

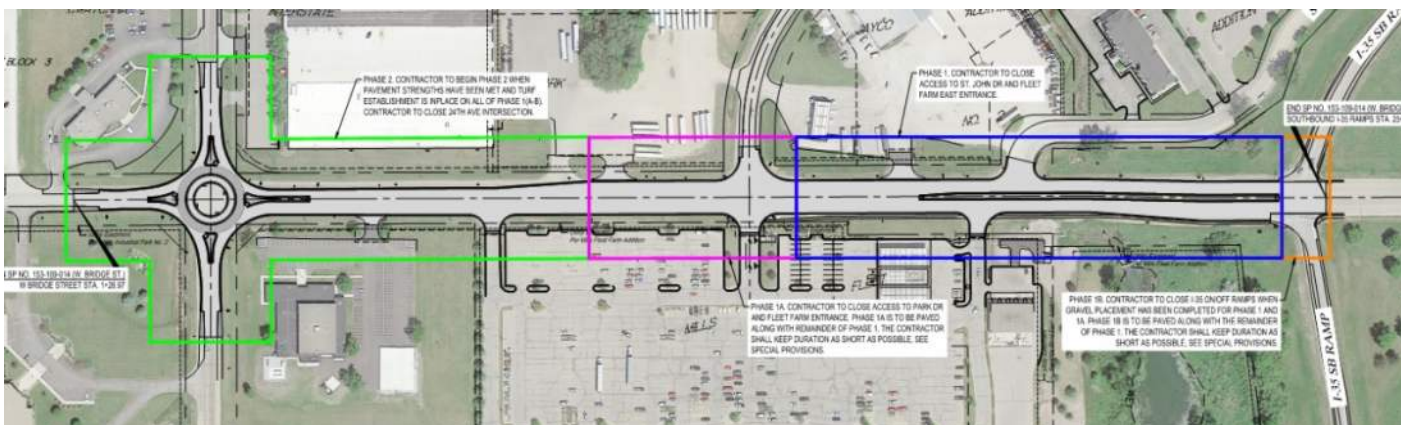

## PROJECT SUMMARY

### Construction Summary

- Construction Start Date: May 3, 2021
- Estimated Completion for current Phase: July 23, 2021
- Estimated Completion for Overall Project: October 30, 2021

## PROJECT CONTACTS

DIRECTOR OF PUBLIC WORKS / CITY ENGINEER

Kyle Skov, P.E.  
City of Owatonna

ON-SITE INSPECTOR (ISG)

Anthony Lance  
Construction Administrator  
Anthony.Lance@ISGInc.com

PROJECT MANAGER (ISG)

Reese Sudtelgte, P.E.  
Civil Engineer  
Reese.Sudtelgte@ISGInc.com
